CTG-GIS DATA SHEET

Chapman Technical Group
a division of GRW

200 Sixth Avenue
Saint Albans, WV 25177

304.727.5501

Buckhannon, WV
Lexington, KY


PROJECT #: 25026.1 **PROJECT NAME:** SAMUC GIS

DATE: 10-29-26 **CREW:** JDRIGGS/JBROWN

CROSS STREET OR ADDRESS lat: 38-23-16.0 long: 81-49-54.6

POINT (STRUCT#) 4405 **STRUCT. TYPE:** (MH) SSMH DI CB CULV CI

TYPE: Brick **DIMENSION:** 2' **CONDITION:** Good **SURFACE:** Asphalt

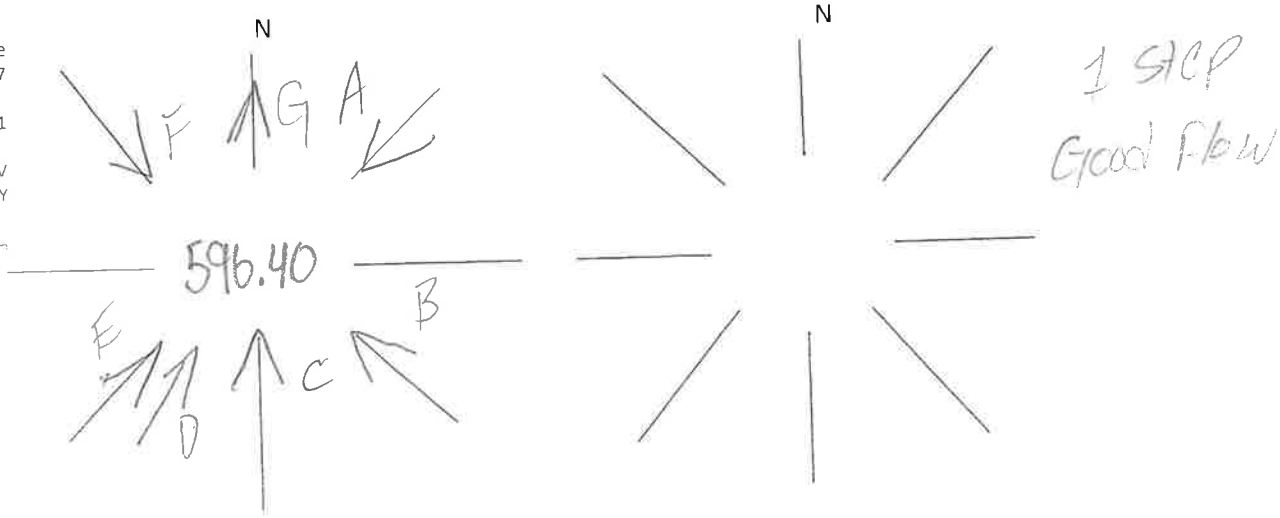

INV LABEL	SIZE	TYPE	MD TO INV	CONNECTS TO	ELEV OF INV
A	6	VCP	-5.83	?	590.57
B	12	VCP	-7.35	?	589.05
C	12	VCP	-14.33	?	582.07
D	4	VCP	-4.42	?	591.98
E	4	VCP	-2.92	?	593.48
F	6	PVC	-4.16	?	592.24
G	12	VCP	-14.45	4411	581.95

~~SW: 4th @ RR Xing~~

* ~~Traffic Control~~
